PROJEK LEBUHRAYA PAN BORNEO SABAH FASA 1B MEMBINA JALAN DARI SARANG KE TEMUNO (WP12)

Setting-out coordinate check (horizontal / level)

SETTING-OUT CHECK RECORD

REF. NO. **WP12-SOC-CST-SSU-20261019-1** DATE **2026-10-19** REVISION **0**

RESULT

FAIL

11 of 12 checked points PASS - 1 FAIL

12	11	1	30.1
POINTS	PASS	FAIL	MAX RADIAL MM (P10)

CHECK DETAILS


REF. NO.	WP12-SOC-CST-SSU-20261019-1	DATE	2026-10-19
RFI NO.	-	TEAM	CST
STRUCTURE	-	CHAINAGE / LOCATION	-
ELEMENT / DESCRIPTION	Kerb line	CHECK TYPE	Horizontal (E, N)
TOLERANCE	H 20 mm (radial)	COORDINATE SYSTEM	GDM2000 / RSO Borneo (BRSO)
TOLERANCE SOURCE	Indicative values only - confirm against approved ITP / Method Statement / JKR Standard Specification for Road Works (JKR/SPJ).	INSTRUMENT / S/N	-
STATION / BACKSIGHT	-	CALIBRATION DATE	-

RESULTS

No	Point	Design		Measured		Offset (mm)			Result	Remarks
		E (X)	N (Y)	E (X)	N (Y)	dE	dN	Radial		
1	P01	612345.000	654321.000	612345.003	654320.998	+3.0	-2.0	3.6	PASS	Within tolerance
2	P02	612347.400	654321.000	612347.396	654321.005	-4.0	+5.0	6.4	PASS	Within tolerance
3	P03	612349.800	654321.000	612349.806	654321.001	+6.0	+1.0	6.1	PASS	Within tolerance
4	P04	612352.200	654321.000	612352.202	654320.997	+2.0	-3.0	3.6	PASS	Within tolerance
5	P05	612345.000	654323.400	612344.995	654323.396	-5.0	-4.0	6.4	PASS	Within tolerance
6	P06	612347.400	654323.400	612347.418	654323.407	+18.0	+7.0	19.3	PASS*	H within tolerance (97% of 20 mm)
7	P07	612349.800	654323.400	612349.804	654323.402	+4.0	+2.0	4.5	PASS	Within tolerance
8	P08	612352.200	654323.400	612352.198	654323.406	-2.0	+6.0	6.3	PASS	Within tolerance
9	P09	612345.000	654325.800	612345.001	654325.799	+1.0	-1.0	1.4	PASS	Within tolerance
10	P10	612347.400	654325.800	612347.372	654325.811	-28.0	+11.0	30.1	FAIL	H exceeds tolerance by 10.1 mm - move 28 mm E, 11 mm S
11	P11	612349.800	654325.800	612349.805	654325.804	+5.0	+4.0	6.4	PASS	Within tolerance
12	P12	612352.200	654325.800	612352.203	654325.794	+3.0	-6.0	6.7	PASS	Within tolerance

dE = Measured E - Design E, dN = Measured N - Design N, Radial = sqrt(dE^2 + dN^2). PASS* = within tolerance but over 80% of it. Coordinates in metres, offsets in mm.

POINT ERROR DISTRIBUTION

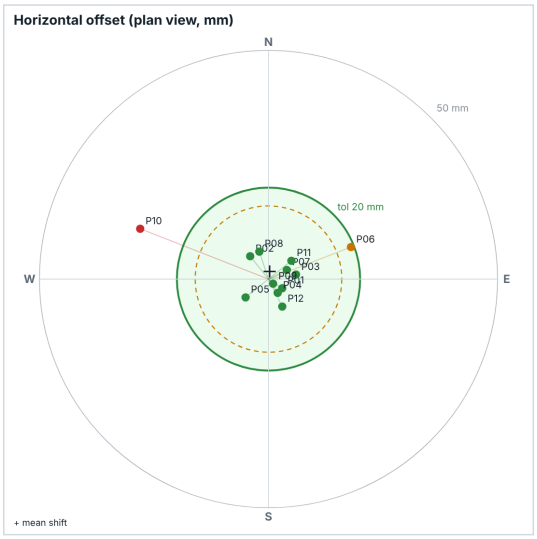

SUMMARY

Points	12
Pass	11 (1 marginal)
Fail	1

HORIZONTAL (MM)

Max radial	30.1 (P10)
Mean radial	8.4
RMS radial	11.4
Mean shift dE/dN	+0.3 / +1.7

NOTES

Prism height 1.500 m. Points re-set after first check.

SIGN-OFF

PREPARED BY

SSU

Surveyor (CST)

SIGNATURE (OPTIONAL) · 2026-10-19

CHECKED BY

SCH

-

SIGNATURE (OPTIONAL) · 2026-10-19

Scan to open the app

Generated document — no signature required. Physical signatures may be added after printing if required.

Checking aid only: this report is generated from user-provided inputs and is not acceptance or certification. The user is responsible for independently verifying source data, point identity, units, coordinate and vertical datums, tolerances and results against approved project documents and field observations before use.
